


RT-12F Refrigeration Trailer


1. Top View

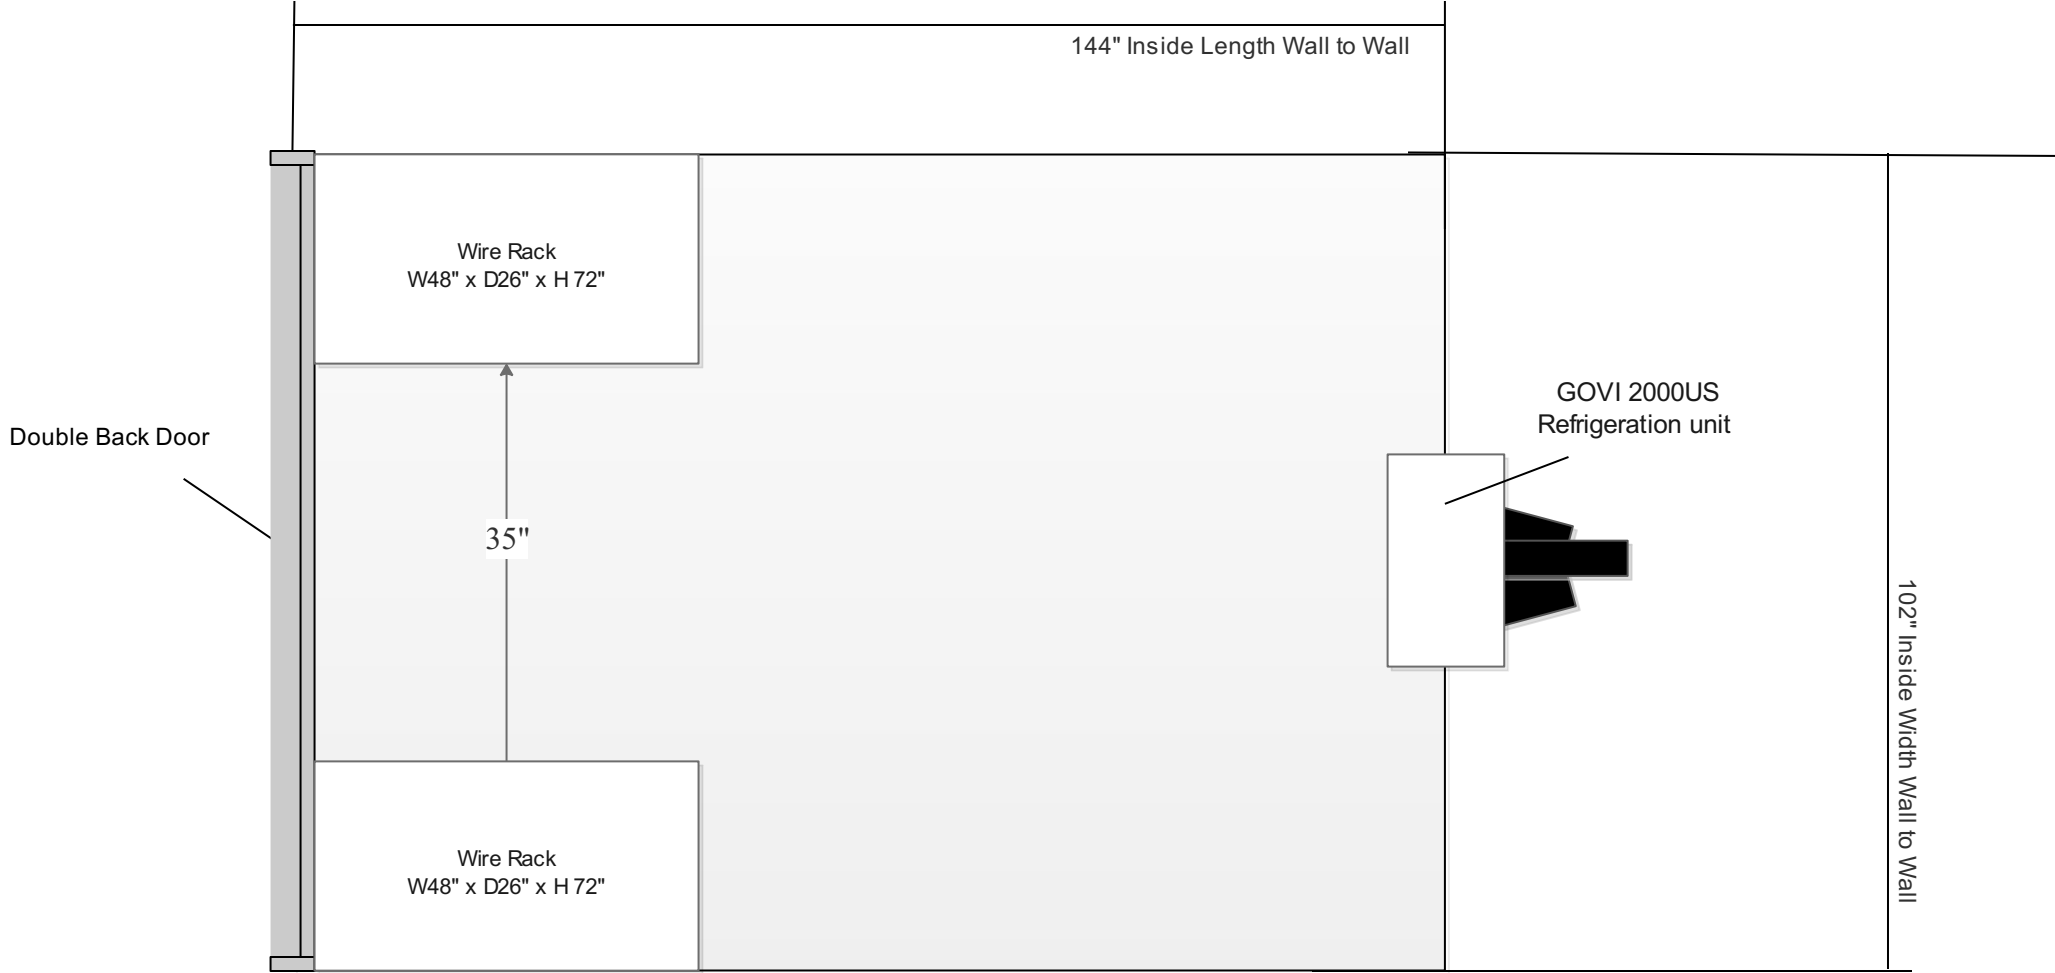

- Description:**
- All submitted plans are scaled of 1/2"=1'
 - 1/8" Aluminum diamond plate will be used for the floor.
 - NSF approved food graded silicon will be used to fill connections of cabinets, walls etc.
 - Aluminum diamond plate floor will be welded to fill gaps and connections to make it water resist
 - Trailer inside height is 84"
 - Shatterproof LED light will be used
 - All equipment mounted securely to the framing structure and/or counter top.

**RT-12F
Refrigeration Trailer**

2. Passenger Side Interior View

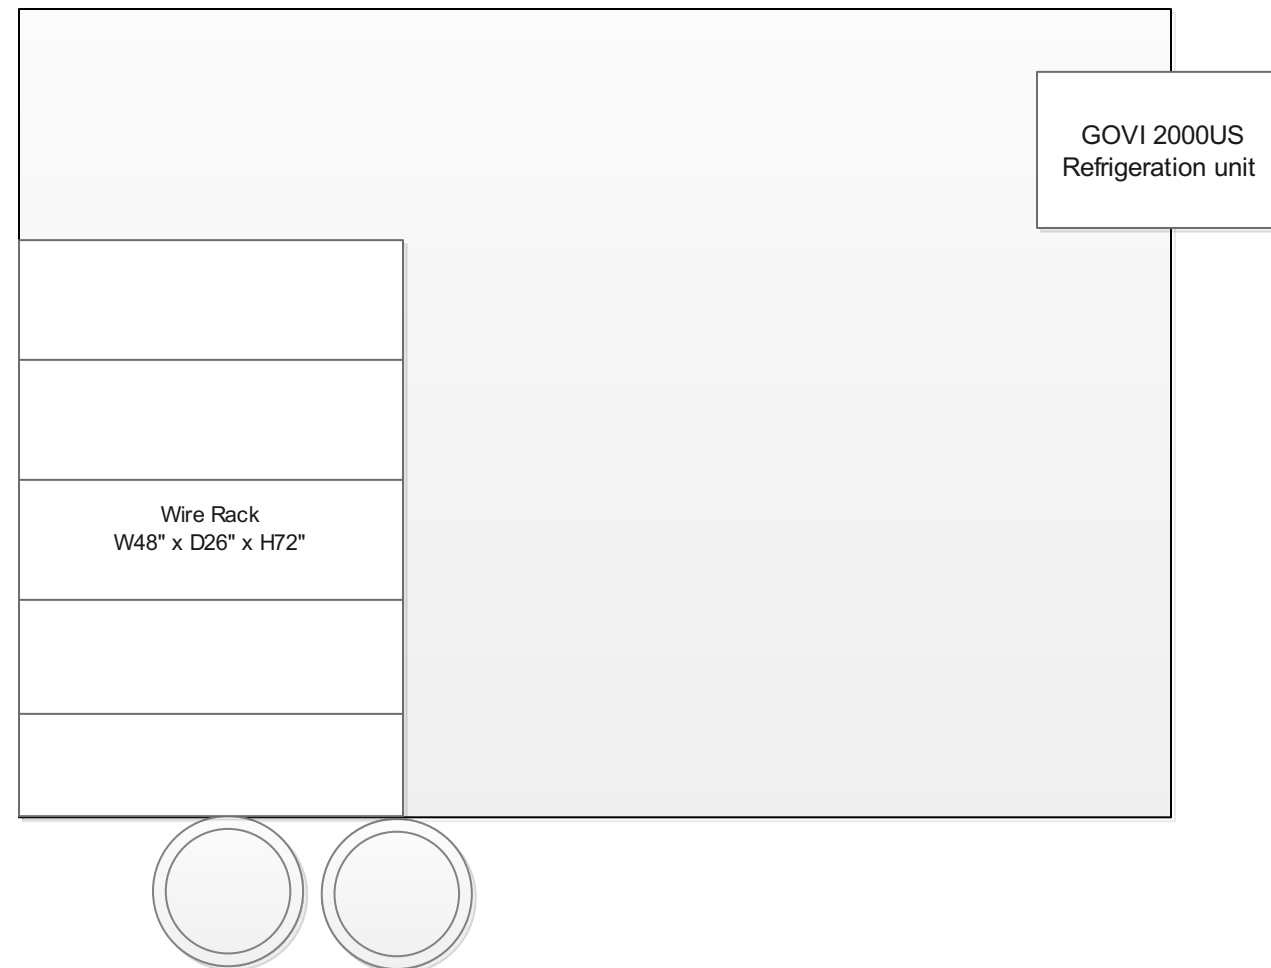


3. Passenger Side Exterior View




**RT-12F
Refrigeration Trailer**

4. Driver Side Interior View

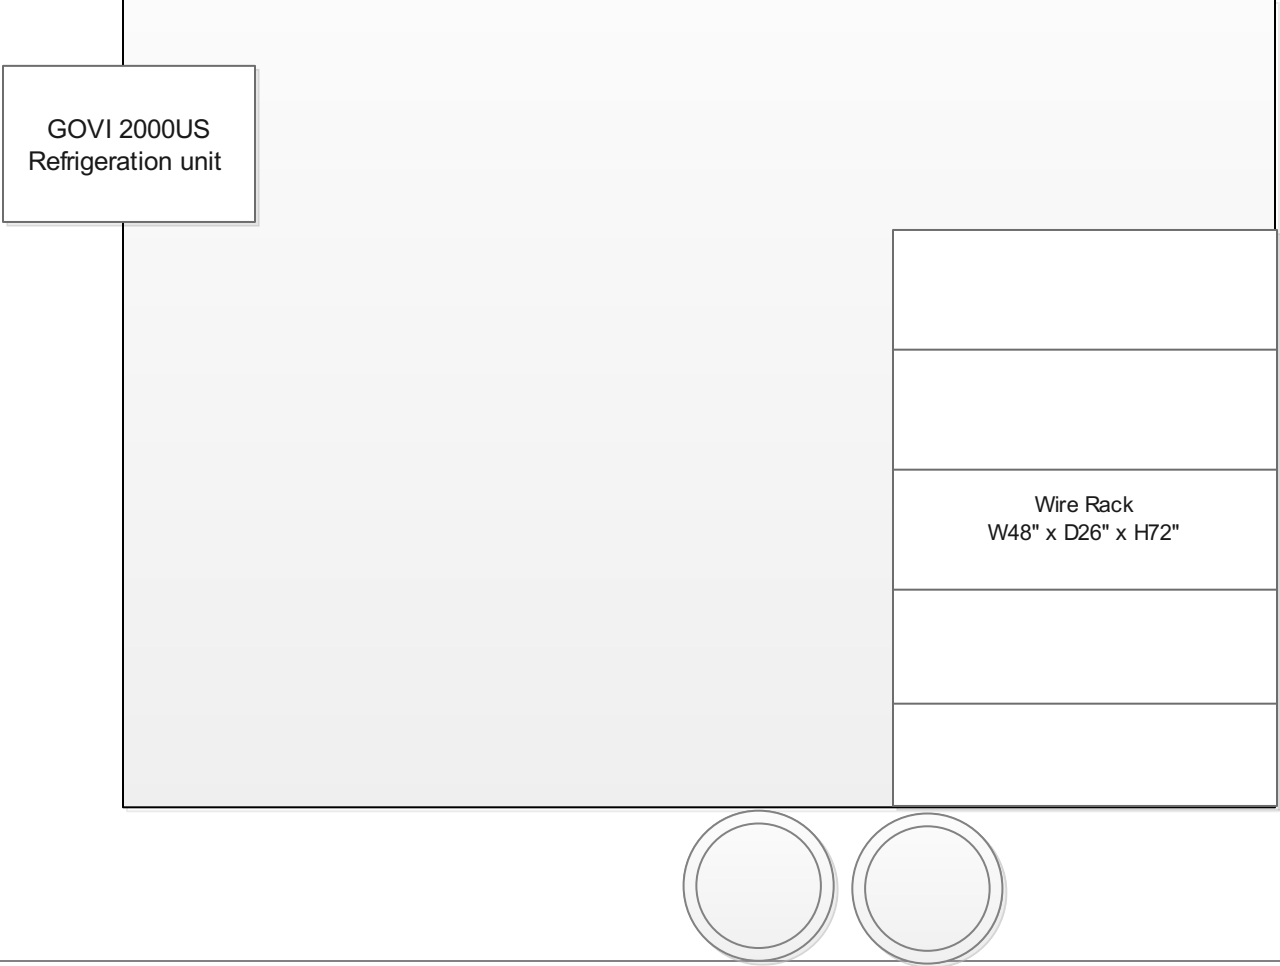


**RT-12F
Refrigeration Trailer**

5. Driver Side Exterior View

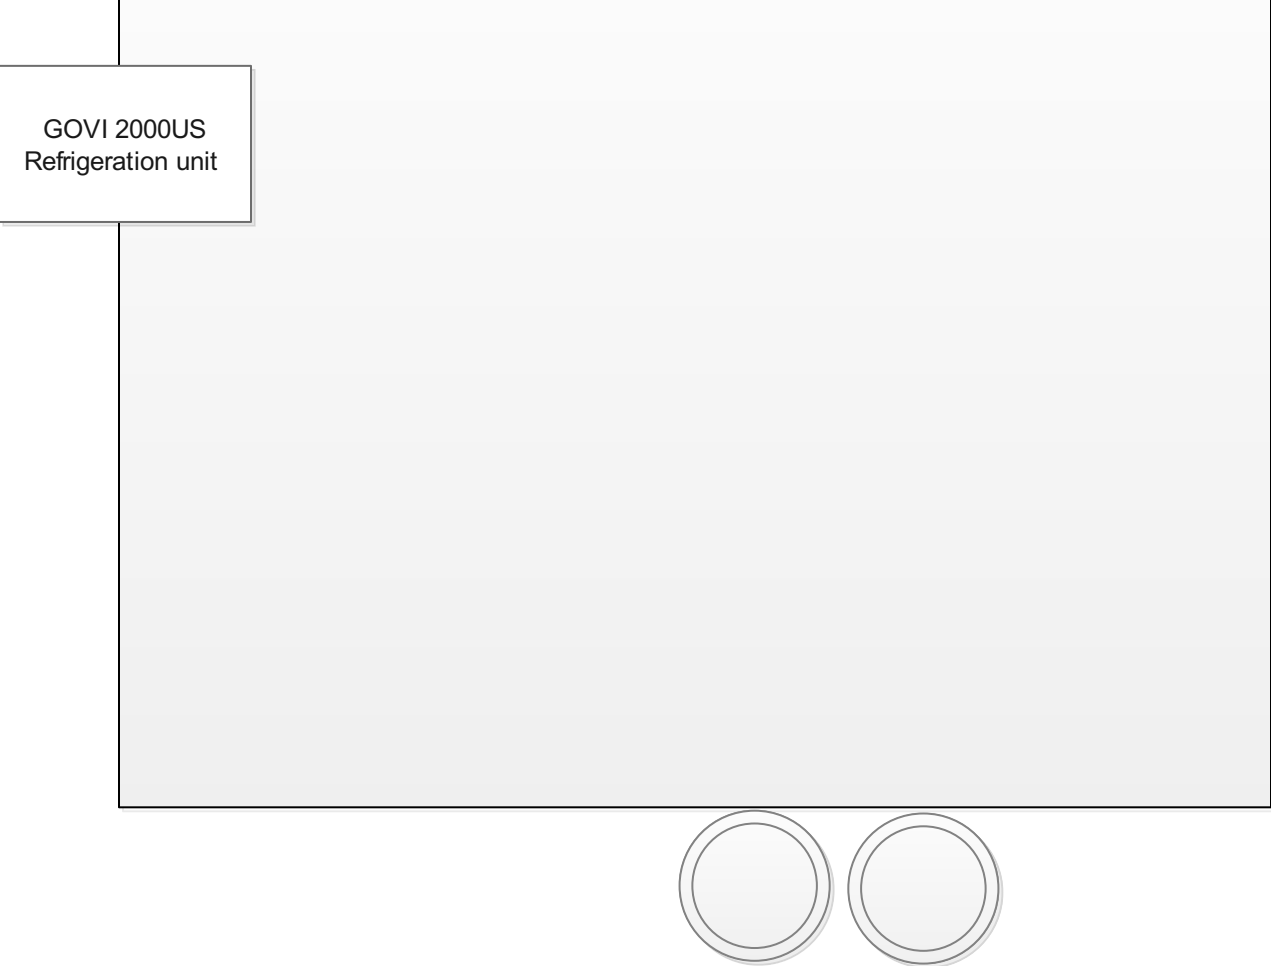

**RT-12F
Refrigeration Trailer**

6. Front Side Exterior View

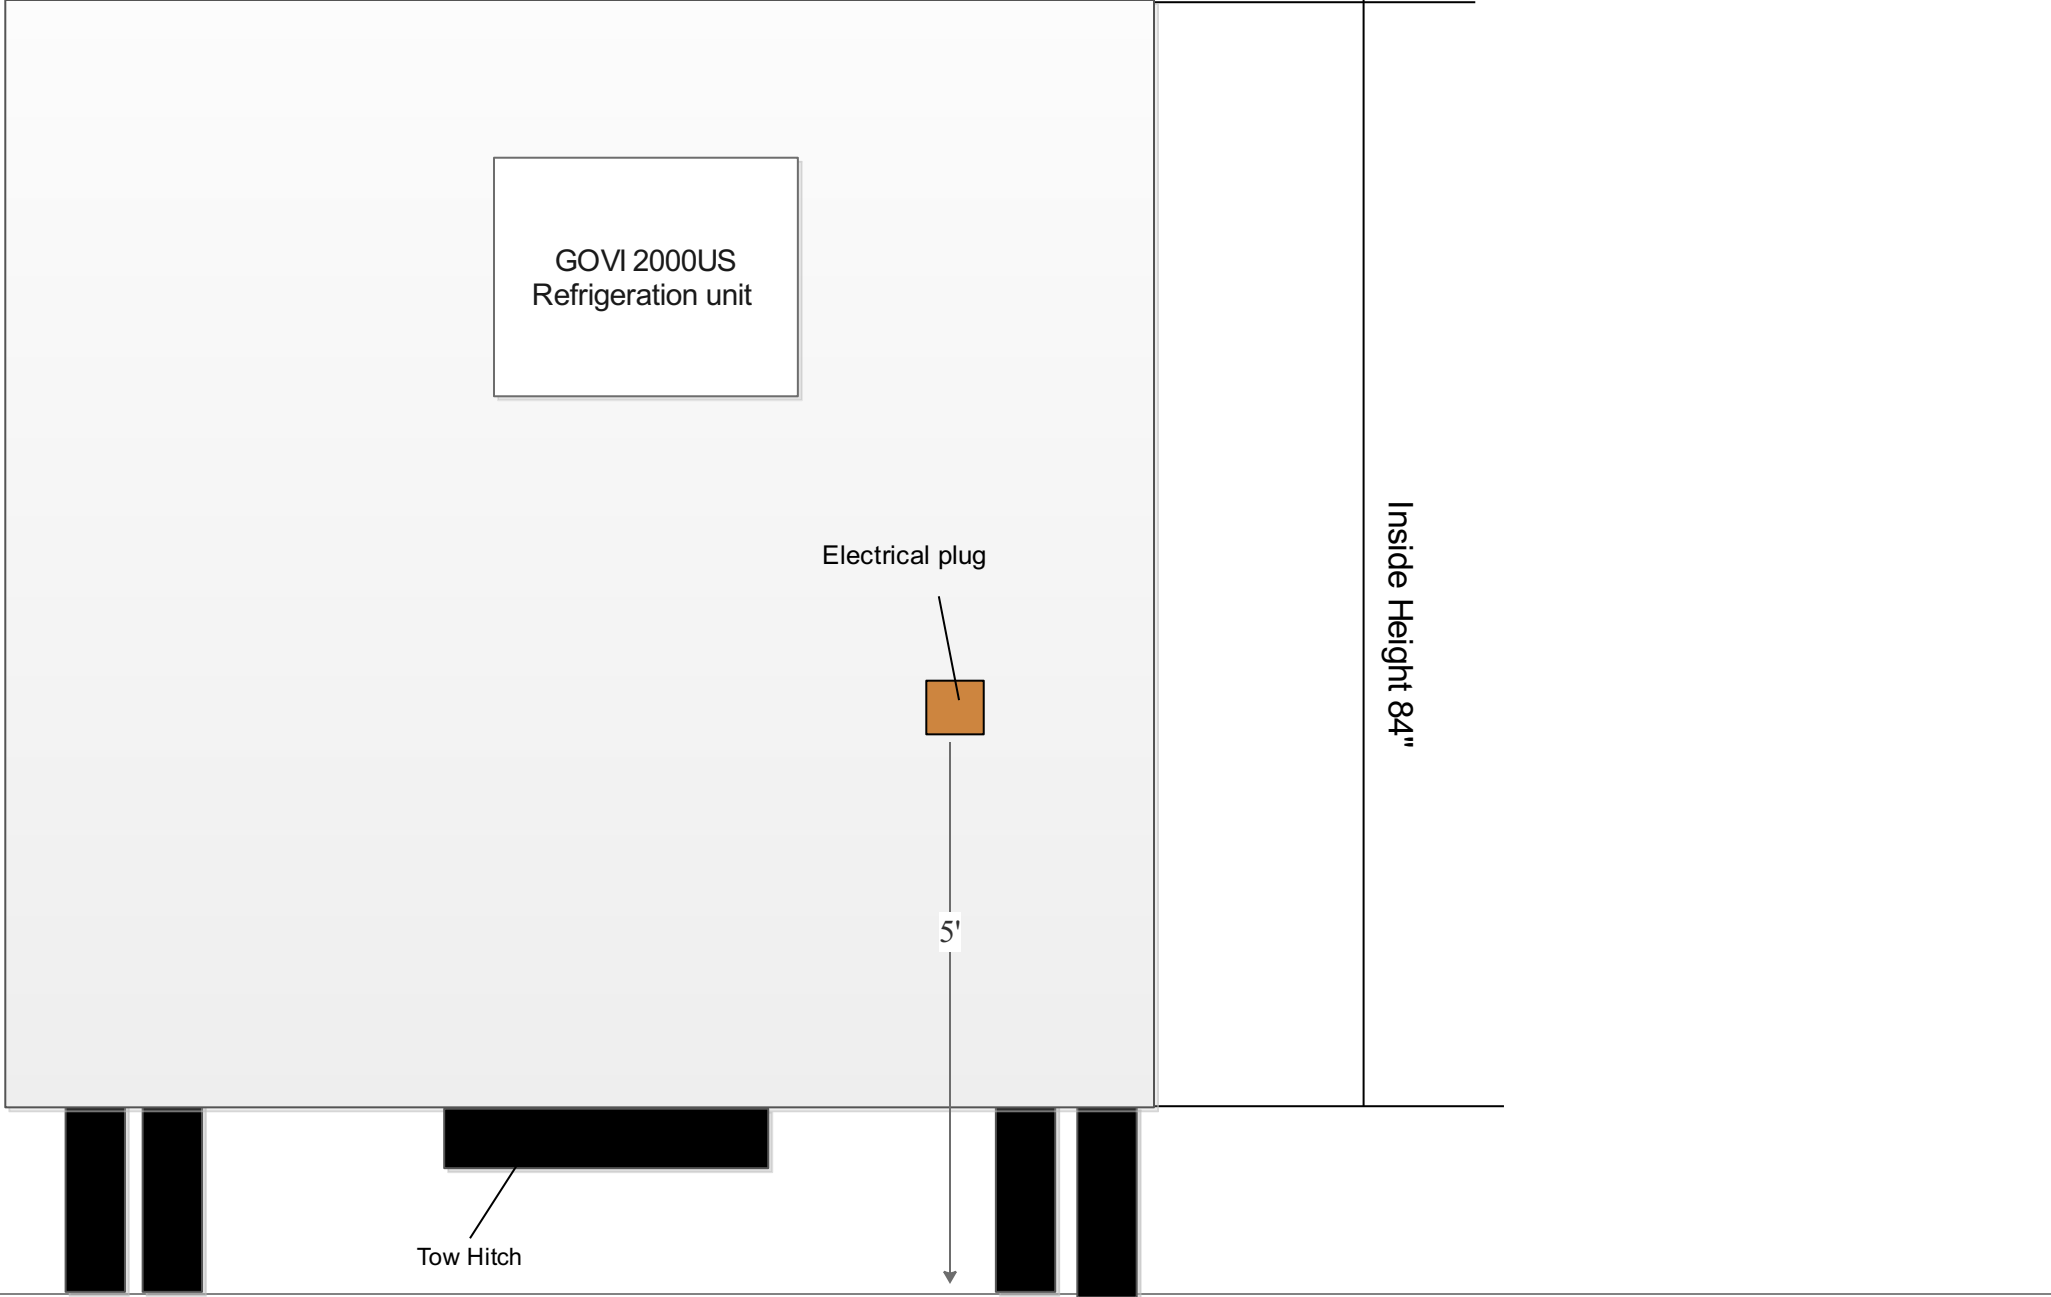



T.R. ARNOLD & ASSOCIATES, INC.

• Engineering • Plan Review • Inspection •

INSPECTION REPORT

Work Order No. 25-00949

Manufacturer : LA Stainless Kings Client No. 7219 Date: 2/24/2025

Plant Address : 8926 Comanche Ave Chatsworth CA 91311

Inspector : Greg Edwards Accompanied By : Tekla Horvath

Rate of Production : 2 Per Month Labels Controlled by : Manufacturer TRA

For Office Use Only Defects Logged <input type="checkbox"/> Red Tags Logged <input type="checkbox"/> Inspection Logged <input type="checkbox"/> Reviewed By : _____ Comments : _____	Inspection Emphasis : Structural <input type="checkbox"/> Plumbing <input checked="" type="checkbox"/> Heating <input type="checkbox"/> Electrical <input checked="" type="checkbox"/> Fire Safety <input checked="" type="checkbox"/> Records <input checked="" type="checkbox"/> Remedial Level : REG	Material Storage Lumber <input type="checkbox"/> Trusses <input type="checkbox"/> Plywood <input type="checkbox"/> Particle Board <input type="checkbox"/> Insulation <input checked="" type="checkbox"/> Doors <input checked="" type="checkbox"/> Windows <input checked="" type="checkbox"/>	Tests Observed Gas High Pressure <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> Gas Low Pressure <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> Electrical Continuity <input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> Electrical Operational <input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> Electrical Polarity <input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> Dielectric Strength <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> Water Supply <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> DWV <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> Fixture <input type="checkbox"/> <input type="checkbox"/> <input checked="" type="checkbox"/> Egress Window Operation <input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> Equipment <input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>
	All Deficiencies Reinspected? Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/>		
	Labeled Yard Units Reinspected? Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/>		
	Unlabeled Yard Units - Checked Status of Q. C. Records? Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/>		
	All other units re-inspected for deviations noted on previous 402/s? Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/> Serial Number of Unit Tested : _____		

INSPECT AND RECORD ALL UNLABELED YARD UNITS AND DEVIATIONS ON FORMS 401 and 402

Station	Serial Number	Model	Approval Number/Date	Destination
Final	N013980	Reefer Trailer	Visual	Model RT-16H
	SPCM 41999			Address:
				9150 Harvest Way Atascadero
				CA 93422
				VIN # 7TKBE1618SN013980
Final	N013979	Reefer Trailer	Visual	Model RT-12F
	SPCM 42000			Address:
				9150 Harvest Way Atascadero
				CA 93422
				VIN # 7TKBE12114SN013979
		These two unit's		
		Don't have gas or water		



T.R. ARNOLD & ASSOCIATES, INC.

• Engineering • Plan Review • Inspection •

INSPECTION OBSERVATION REPORT

Form 402
Issued 03/21/2012
Revised 05/11/2022

LA Stainless King Chatsworth CA 91311

12/13/2024

MANUFACTURER AND PLANT LOCATION

Date

Page 2 Of 2

SERIAL NUMBER	DAPIA/CCI/MCI CODE REF.	OBSERVATIONS/COMMENTS
N013980		This was a Final California SPCM Inspection of two Refrigeration Trailer's under title 25 Chapter three Article
N013979		Under title 25 Chapter three article 3
		Items checked:
		Egress doors, Insulation, refrigeration equipment, electrical panel box, lighting, exit sign.
		These two units are only for refrigeration. No plumbing or gas system.
		Intro and exit meeting with LA Stainless Kings representative.
		This Inspection does not cover steps, ramps, handrails or foundation.

I have reviewed the issues presented and instituted procedures for correction of non-conforming items.

Greg Edwards

Manufacturers Representative

The above report is a true and accurate account of the issues noted to the best of my knowledge.

Tekla Horvath

Inspector

Time In 12:30 Time Out 2:30

Inspection time 2

• 4703 Chester Drive • Elkhart, IN 46516 •
• Phone (574) 264-0745 • Fax (574) 264-0740 •
• www.trarnold.com •
